

EFEO REACH PROGRAM
LEARNINGS PHASE 1
for
PHASE 2

Hans van Bergen

EFEO REACH PROGRAM

LEARNINGS PHASE 1

for

PHASE 2

START NOW PHASE 2, DO NOT WAIT !

LEARNINGS PHASE 1

1. Organisation:
 - a. Consortium Agreement
 - b. Roles & Responsibilities
 - c. Cost Sharing Structure

In place
2. Expertise / Resources

Limited
3. Contracts with Consultants / WGA Trustee

Takes Time
4. Sameness Check (substance identification)

Complex
5. Data Collection / Evaluation / Access

Complex

 - a. Several agreements

Takes Time
6. Additional Testing & Contracts

Takes Time
7. Dossier / CSR Preparation:
 - a. Lead Registrant

Complex
 - b. Other Registrants

Takes Time

PHASE 1: *March 2008 – Dec. 2010*

MILESTONES

M
O
U

Lead Reg.
&
members

Consort. Agreem.

RHK project agreem.
WGA trustee agreem.



RHK Exposure CSR 2x

Data owner agreem.
RIFM, Companies

Data gaps testplan
Letter of Access

LR submission

Other submissions

03/08

05/09

07/09

11/09

03-4/10

09/10 12/10



- sameness check
 - data review
 - IUCLID training
 - Pilot dossiers

Funding
& admin


* RHK Dossier preparation
* Guidance Chapter 1 - 3



E.F.E.O.
European Federation of Essential oils

PHASE 2: *June 2010 – June 2013*

PLANNING

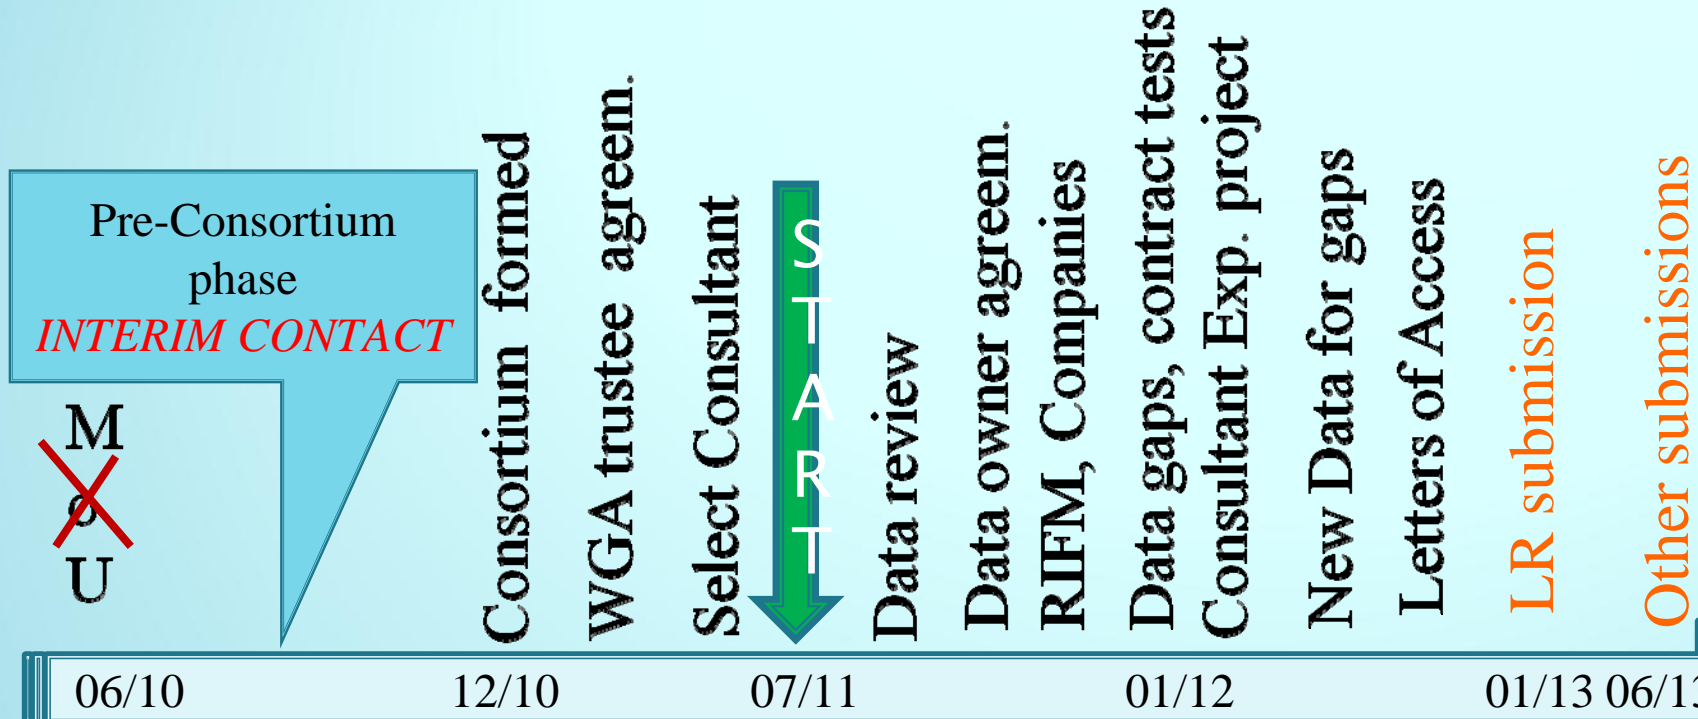

Funding & admin.
WGA agreed

- sameness check
- data review
- data collection

* Dossier prepared by consultant
* Companies prepare reference dossiers



PHASE 2: 8 NCS GROUPS

TOTAL OF RESPONDING COMPANIES: 33

(counting an organisation with multiple representations as ONE)

CONSORTIUM	NUMBER NCSs	NCSs ADDED by RESPONDENTS	TOTAL NCSs	NCSs for 2013	NUMBER of COMPANIES	NCSs with VOLUNTEER LEAD REG. for 2013	VOLUNTEER COORDINATOR	EFEQ INTERIM PRIMARY CONTACT
LINALOOL / LINALYL ACETATE	9	1	10	6	28	1	Y	francis951@aol.com
CARVONE	7	1	8	2	19	0		jens-achim.protzen@kaders.de
CINNAMATES	3	0	3	0	12	0		f.peter.meschede@ramex.de
CITRAL / CITRONELLAL	5	2	7	1	19	0		slluch@lluche.com
PINE	7	5	12	2	16	2		rolf.storm@eu.sensient-tech.com
SESQUITERPENE H.C. & ALCOHOLS	15	11	26	6	23	2		laure.moutet@kerry.com
THUJONE	5	1	6	1	12	1		bertrand.depreville@biolandes.com
CINEOL	6	1	7	2	22	0		tduclos@quimdis.com
NUMBER OF NCSs	57	22	79	20		6		

(6 x one company)

PHASE 2: EFEO INTERIM CONTACT

	TASK	COMPLETION DATE in 2010	EFEO	REACH CONSULTANT	EFEO-IPC
1	<u>1st communication:</u> EFEO announcement	Febr. 16	x		
2	Company inquiries	Febr. – March and thereafter	x	Background support	x
3	Prepare pre-consortium candidate list with -Companies ,contacts, their NCSs -volunteers for roles	March 31	x	review	Review & approval
4	<u>2nd communication:</u> List of companies (not yet their NCSs) per pre-consortium to applicants with -letter on procedure	June 2010 (additions / deletions July)	x	x (letter)	Review & approval
5	Adjustment of list of pre-consortium members with their NCSs and volunteers	August 30	x	review	Review & approval
6	<u>3rd communication:</u> Announcement pre-consortium joint webinar 2 nd part of June with -list of members, their NCSs, agenda, consortium model agreement	Announcement end of August 2010, Webinar 2 nd half September	x	Arrange agenda with EFEO & IPCs and prepare webinar	* Approve agenda and select date * participate to webinar * inventory for need of one-to-one calls/ conf calls/meetings
7	Consortia formation by collecting signatures and assign roles of responsibilities	Oct – Nov 2010		support	* Transfer IPC role to pre-consortium Lead Company
Interim Primary Contact transfers tasks to:					LEADCOMPANY
8	<u>4th communication:</u> Announcement of consortia and constitutional meeting -Agenda, membership, roles & responsibilities, NCS ownership, first roadmap	December 30		Prepare agenda with Lead Companies	Preparation and Chair : -lead company or -other interim chair
9	December 31st , Consortium in place to start work on sameness, etc.				



EFEO REACH PROGRAM

LET US APPLY THE LEARNING

OF PHASE 1 for PHASE 2

START NOW, DO NOT WAIT!
